

Olera Pre-CRP R&D, Commercialization, and Execution Plan

September 2026–January 2027

1. PURPOSE

The objective before the January 2027 CRP submission is to retire the major weaknesses exposed by our August/September drafting and mock-review process. We have a strong understanding of the problem, a compelling innovation, and a clear vision for modeling the care-establishment pathway and creating solutions for the steps along that pathway.

The next 18 weeks should therefore retire risk and produce evidence before submission: demonstrate that we can commercialize products within the eldercare ecosystem; complete and validate a substantially mature first-generation CareNavigator; use institutional-buyer discovery to refine the CRP research strategy and evidence requirements; and establish an investable post-CRP path.

2. STRATEGIC MODEL

Olera operates within the eldercare ecosystem around a care-establishment pathway that moves an older adult or family from an identified need to established care and measurable outcomes. Failure at any step can return the family to unmet need and the downstream vicious cycle. CareNavigator is the end-to-end product intended to make that full pathway navigable, executable, measurable, and progressively more reliable.

Before CareNavigator reaches full commercial maturity, Olera can commercialize narrower provider products at specific high-value pathway steps. Client Growth addresses the Find Care step by helping providers acquire and convert appropriate clients; Caregiver Staffing addresses the Staff Care step by helping providers recruit and place workers. These products improve the same pathway, create near-term revenue without charging families, demonstrate that the team can commercialize with ecosystem stakeholders, and deepen the provider records, relationships, workflows, and operating knowledge that CareNavigator will ultimately use.

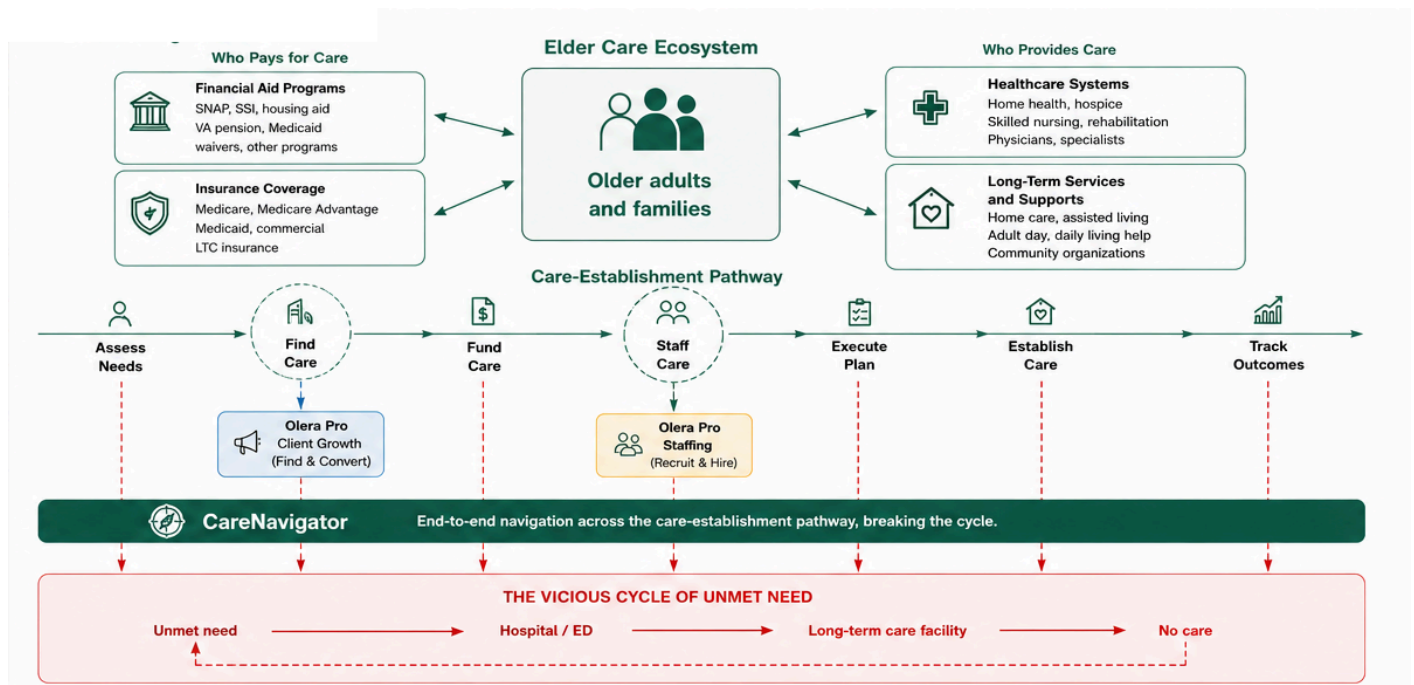


Figure 1. Olera's strategic model: the eldercare ecosystem, care-establishment pathway, provider-product beachheads, CareNavigator, and the vicious cycle of unmet need.

3. OLERA R&D AND COMMERCIALIZATION ROADMAP

The CRP is one component of a broader R&D and commercialization program. The near-term work should leave Olera entering CRP with a mature first-generation product, commercial execution evidence, and buyer-informed late-stage R&D objectives.

Stage / Timeframe	Primary work	Outcome	Handoff
Phase I & II 2021–2024 COMPLETE	Problem definition; national data; assessment/navigation foundation; provider ecosystem pilots.	Foundation, data assets, early providers, and core innovation established.	Completed.
Phase IIB / Pre-CRP 2024–2026 WE ARE HERE	First-generation CareNavigator; ~n=200 family usability/V&V study; provider commercialization along the pathway; institutional-buyer discovery.	Mature first-generation product + feasibility evidence + commercial execution + buyer-informed CRP plan.	Ready for CRP Day 1 with a mature product and defensible evidence requirements.
CRP / Late-Stage R&D 2027–2030	Second-generation development; design and quality-systems improvement; buyer-informed rigorous real-world validation.	Defensible evidence that closes remaining technical and commercialization risks for CareNavigator.	Evidence package supporting post-CRP institutional proof of concept.
Post-CRP / Scale 2030+	Paid institutional proof of concept; scale contracts; expand provider products and platform.	Demonstrated utilization/economic value, revenue scale, and durable infrastructure.	Scale with non-SBIR capital.

Table 1. The R&D and commercialization program. What each stage does, what it produces, and what it hands to the stage after it.

4. PHASE IIB / PRE-CRP OBJECTIVES

The remainder of Phase IIB should focus on three parallel objectives. Together they retire the commercial-execution, technical, and commercial-thesis risks that weakened the first CRP draft.

A. Provider commercialization: retire commercial-execution risk. Use company resources to commercialize narrow products at identified pathway steps, beginning with non-medical home care agencies. The goal is not to make these provider products the CRP-funded technology. It is to prove that Olera can sell, deliver, retain, and generate revenue with stakeholders in the same ecosystem in which CareNavigator operates.

Product	Working offer / target	What it teaches or builds	Commercial evidence
Olera Pro Client Growth	Working hypothesis: ~\$100–\$150/month; target ~25 agencies. Managed ads, provider pages, lead qualification/conversion, reviews, and SEO.	Provider acquisition and conversion workflows; richer provider records; demand and referral knowledge.	Paying accounts, repeat purchasing/retention, revenue, delivery cost.
Olera Pro Staffing	\$250 per successful hire; target ~25 agencies averaging ~3 hires/month.	Workforce capacity at the Staff Care step; provider staffing demand; student-worker supply and placement workflows.	Paid hires, repeat purchasing, retention, unit economics.

Table 2. The two provider products. Pricing and targets are working hypotheses until the team locks them, as the paragraph below states.

At the working targets above, the two products could create a meaningful pre-submission revenue run rate. The exact target should be treated as a planning hypothesis until the team locks pricing and the beachhead. The strategic value is broader than the revenue itself: the work retires team execution risk and strengthens the network, records, and operating knowledge required for CareNavigator.

B. CareNavigator first-generation development: retire technical risk. Phase IIB should deliver the first end-to-end CareNavigator before CRP Day 1. The system should assess needs, identify care and funding options, construct a plan, execute bounded administrative workflows through permission-gated agents, verify whether care is established, track outcomes, and persist the pathway data needed for learning.

The planned ~n=200 Phase IIB family study should be used primarily to establish usability, feasibility, workflow performance, safety/verification, and whether the first-generation system functions as specified across real navigation episodes. This should retire the basic technical question of whether the product exists and works well enough to justify late-stage development, rather than asking CRP to fund creation of the first functional product.

Pre-CRP period	CareNavigator work	Required output
September	Lock first-generation requirements; map end-to-end pathway states; define execution-agent boundaries, data capture, verification, and safety controls.	Frozen first-generation requirements and V&V plan.
October	Complete core end-to-end engineering and execution workflows; instrument state transitions, actions, exceptions, and outcomes.	Study-ready first-generation system.
November	Run/continue ~n=200 family usability and V&V study; resolve critical failures; document workflow performance.	Usability, feasibility, safety, and workflow evidence.
December	Freeze evidence; document specifications and remaining technical risks; translate findings into CRP second-generation design and quality-system work.	Mature first-generation product and CRP-ready technical evidence package.

Table 3. The pre-CRP CareNavigator plan, month by month, and the output each month has to produce.

C. Institutional-buyer discovery: retire commercial-thesis risk. Buyer discovery should test rather than assume the institutional CareNavigator thesis. We need to determine whether Medicare Advantage plans, ACOs, and other risk-bearing organizations view failed care establishment as a sufficiently important and addressable driver of utilization; how they solve the problem today; what alternatives already exist; what economic value successful care establishment could create; what they would pay for; and what evidence would be required before a paid proof of concept.

Question	What we need to learn before CRP	Desired output
Problem and value	Does improving care establishment matter enough to buyers? What utilization/cost mechanisms matter?	Validated or rejected value proposition.
Competition	How is this solved today? Where are existing vendors or internal programs strong or weak?	Clear differentiation and whitespace.
Economics	What population, contract structure, price logic, and savings threshold would matter?	Initial commercial and POC economics.
Evidence	What endpoints, comparison design, data, sample, follow-up, and decision thresholds would support a post-CRP POC?	Buyer-informed CRP evidence requirements and POC specification.

Table 4. What institutional-buyer discovery has to resolve before the CRP, and the output that resolves each question.

5. PRIVATE INVESTORS AND THE LONG-TERM THESIS

Private investors would be investing in Olera's full R&D and commercialization program over the next several years for a potentially much longer-term upside. The thesis is that Olera can become infrastructure for the care-establishment pathway within a growing eldercare ecosystem: building the data, provider relationships, workflows, execution tools, and navigation layer that help families move from need to established care while reducing costly downstream failure.

Near-term provider products matter because they can generate revenue now, prove commercial execution, and deepen the network while CareNavigator matures. CareNavigator creates the larger potential upside if better care establishment can be shown to reduce avoidable utilization and create economic value for risk-bearing buyers. Over time, a sufficiently instrumented pathway could also become a platform into which new care-delivery technologies, including automation, AI, and robotics, can be incorporated as the underlying care ecosystem evolves.

The pre-CRP investor objective is therefore not simply to obtain supportive letters. It is to make the thesis diligence-ready: demonstrate execution, show a functioning first-generation CareNavigator, validate institutional demand and evidence requirements, and present a credible financing path from CRP through proof of concept and scale.

6. RISKS TO RETIRE BEFORE THE CRP SUBMISSION

This is the January scorecard. Targets are planning goals, not facts; the final application should only make claims supported by evidence actually achieved.

Risk	Why it matters	Target	Stretch	What we could say in the CRP if achieved
Commercial execution	Reviewers need evidence that the team can sell and deliver.	Paying provider customers; repeat purchasing; documented revenue/unit economics.	Broader provider base and stronger recurring revenue.	Olera has demonstrated commercial execution with paying customers and repeat value.
Provider network	CareNavigator depends on responsive, accurate provider infrastructure.	Active providers with updated records and meaningful engagement.	Larger, deeper, geographically concentrated network.	Olera has built and activated a responsive provider substrate supporting navigation.
CareNavigator product	The CRP should begin with a late-stage product, not an early prototype.	First-generation end-to-end system; execution agents; safety controls; tracking.	Full intended first-generation feature set with V&V complete.	The first-generation CareNavigator exists and has been technically validated for late-stage development.
Phase IIB evidence	Reduces technical and feasibility uncertainty.	~n=200 study complete or substantially complete with interpretable usability/feasibility evidence.	Strong usability plus preliminary care-establishment signals.	Phase IIB provides direct feasibility and usability evidence supporting CRP advancement.
Institutional buyers	Determines whether the commercialization thesis and CRP evidence plan are real.	Convergent interviews defining value, endpoints, POC design, and willingness to engage.	Letters/LOIs supporting a post-CRP POC if milestones are met.	Institutional-buyer discovery directly informed the CRP evidence plan and post-CRP handoff.
Private investors	CRP requires a credible path to independent financing.	Investors diligence the thesis; supportive relationships and financing plan.	Formal support and credible post-CRP financing interest.	Independent investors have evaluated the opportunity and support the commercialization path.

Table 5. The January scorecard. What each risk would let the application say if the target is met.

7. 18-WEEK EXECUTION PLAN TO JANUARY 1, 2027

The weekly plan operationalizes the scorecard above. It should remain simple enough to review every week and change when new evidence changes the plan.

Week	Dates	The week's job	Tasks
1	Aug 31–Sep 4	Decide and set the baseline	Lock target/stretch goals; choose beachhead emphasis; record baseline provider, product, buyer, and CareNavigator metrics; stand up weekly dashboard.
2	Sep 7–11	Package the offers	Finalize Client Growth and Staffing offers, pricing, terms, delivery workflow, and target agency list; define what will be measured.
3	Sep 14–18	Start selling; start buyer discovery	Launch concentrated provider outreach; finish institutional-buyer hypothesis/interview guide; book first MA/ACO conversations.
4	Sep 21–25	Lock the pre-CRP product plan	Freeze first-generation CareNavigator requirements and V&V plan; continue sales; conduct first buyer interviews.
5	Sep 28–Oct 2	Close first customers	Close first paying provider(s); continue buyer interviews; review Month 1 against scorecard.
6	Oct 5–9	Make delivery repeatable	Standardize delivery from first customers; continue buyer discovery; complete study-ready CareNavigator workflows.
7	Oct 12–16	Prove repeat value	Convert next provider cohort; pursue first repeat purchase/retention evidence; begin/continue family V&V study.
8	Oct 19–23	Converge on evidence requirements	Synthesize buyer interviews; identify convergent endpoints, data requirements, and POC expectations; revise CRP architecture accordingly.
9	Oct 26–30	Month 2 review	Review traction, CareNavigator development, study progress, and buyer discovery against target/stretch scorecard; correct gaps.
10	Nov 2–6	Use conferences strategically	Meet targeted investors/buyers; test thesis; capture objections and required evidence; continue sales and V&V.
11	Nov 9–13	Convert conversations into commitments	Follow up rapidly; seek concrete next steps, diligence, and conditional post-CRP POC interest where warranted.

Week	Dates	The week's job	Tasks
12	Nov 16–20	Draft the application	Draft Research Strategy and Commercialization Plan from the now-better-supported thesis; identify remaining evidence gaps.
13	Nov 23–27	Hold the line	Maintain sales, study execution, buyer follow-up, and evidence capture through the holiday week.
14	Nov 30–Dec 4	Prove traction	Show retention/repeat purchase; consolidate CareNavigator V&V data; update economics and buyer evidence.
15	Dec 7–11	Lock the evidence	Freeze core traction and study numbers; finalize buyer-informed CRP design; identify final letters/support.
16	Dec 14–18	Everything complete	Complete substantive sections and internal review; assemble letters and supporting materials; finalize scorecard.
17	Dec 21–25	Buffer only	Resolve remaining material gaps; avoid starting new initiatives; proof and reconcile application.
18	Dec 28–Jan 1	Wrap up and submit	Final compliance check; final edits and assembly; submit.

Table 6. The eighteen weeks to submission. One job per week, with the tasks under it.

Working note. This is a living planning memo. We will review progress weekly and adjust targets, tasks, and the CRP strategy as evidence emerges.
