

MedJobs User Success Manager Operations

User Success Manager view of the MedJobs 2.0 operating system · 4 September 2026

A role view of the MedJobs 2.0 Master Implementation Matrix. Every instruction here comes from that document, which stays the source of truth. Nothing has been added to the operating model; where the master leaves a question open, it is marked **GAP / DECISION NEEDED** rather than answered here.

CRM is the workspace label. The operating role is **User Success Manager**, and that is the term used throughout.


ROLE PURPOSE Own the relationship from the moment a provider converts and from the moment an advisor agrees a channel plan, and carry both through to a placement we can bill for. One role holds it across both sides of MedJobs. Chantel is the User Success Manager today.

WHAT YOU OWN PR3 client success. ST3 to ST7 university activation. MA3 hire confirmed. MA4 six or more shifts worked, confirmed. MA5 bill issued and collected. The monthly client list call.

WHAT YOU DO NOT OWN Prospecting, outreach and booking, which are the Admin Team's. The two meetings, which are the Sales Lead's. ST8, QUAL, MA1 and MA2, which the Portal owns. On those four you are the exception handler, not a step in the flow.

WHO HANDS WORK TO YOU The Sales Lead, once the meeting outcome is logged. A converted provider on one side, an agreed channel plan on the other.

WHO YOU HAND WORK TO The Portal. On the provider side, once the account is ready and a staffing need is recorded. On the university side, the moment a student follows the link. The partner row stays open and keeps producing.



WHAT CLIENT SUCCESS IS

The ongoing relationship function, from the moment a provider converts. It is not onboarding, which ends, and it is not support, which waits to be asked. It is one person owning the client from the meeting through the first hire and every hire after: the profile, the terms, the account setup, the interviews, the placements, the six-shift threshold, the invoice, and the next staffing need.

Almost none of this is built. PR3 runs by hand today, and so do MA3, MA4 and MA5. The master describes how it should work and carries every missing piece on the deferred build list. Nothing here is blocked on that; it is blocked on someone doing it consistently.

[Back to top](#)

PR3 CLIENT SUCCESS

Objective Carry the provider from the meeting to a first hire: profile updated, terms understood, account set up and ready for the first student to arrive.

Trigger	The Sales Lead logs <i>Interested / went well</i> on PR2. In the meeting they have already named the handoff: <i>"our user success team will follow up with you on next steps"</i>
Tools	The provider drawer timeline · email, by hand · the provider portal for the profile, chased by hand · Calendly, by hand
Communications	The post-meeting terms email · profile reminders · the setup meeting invitation · everything after it, from the same person
Completion criteria	Profile updated · terms email sent and acknowledged · setup meeting held · the account ready to receive a candidate

Handoff	User Success Manager to the Portal , once the account is ready and a staffing need is recorded. The staffing need drives matching; the client stays yours from here on
----------------	---

REQUIRED ACTIONS

1. **Read the record before you write.** The meeting notes tell you what they asked for and what was promised. Opening with something they said is the difference between a follow-up and a form letter.
2. **Send the terms email within one business day of the meeting**, while it is still fresh for them.
3. **Land three things, in this order:** profile updated, terms understood, setup meeting booked. Chase each until it is done rather than sending one email and waiting.
4. **Book the setup meeting one to two weeks out.** It is the readiness check, the last chance to catch a half-finished account before a student is looking at it.
5. **Write down every touchpoint.** Until the client record exists, keep it on the row so the history stays in one place.
6. **Do not hand a client to the marketplace until the account is ready.** A provider looking at candidates with an incomplete profile gets bad matches and blames the matching.

WHAT MUST BE RECORDED

Terms sent and acknowledged, profile answers and demand profile, setup meeting held, and every touchpoint after conversion.

What is built and what is not. Reading the whole record before making contact is supported by the provider drawer timeline. The profile is partly supported through the provider portal. The terms email, the setup meeting booking and the setup meeting itself are manual. The conversion alert (**B4**) and the client record (**B5**) do not exist.

[Back to top](#)

ST3 TO ST7 UNIVERSITY ACTIVATION

Objective Turn the channel plan agreed in ST2 into five live channels at that university, then keep each one alive.

This stage does not close. Every stage before it ends in an outcome. Activation ends in a standing commitment: postings expire, officers graduate, a career fair moves, a listserv only sends when someone remembers. **Each channel is two motions, secure it once, then keep it alive**, and the second decides whether a university produces students in the spring as well as the fall.

There is no generic version of this stage. One campus is a dead job board and a listserv that reaches everyone; the next is three student orgs and a professor who will give us ten minutes of a class. Work the plan per row, not per channel.

Trigger	The Sales Lead logs <i>Interested / went well</i> on ST2 and hands over the channel plan
Ownership	Yours, with the Sales Lead where a physician in the room changes the answer
Tools	The partner row and its meeting notes · the flyer as the shared asset · ready-to-send copy per channel. The advisor follow-up tab this stage needs does not exist
Communications	Ready-to-send copy per channel · the flyer · the listserv reminder to the advisor · the results-back note · the professor email sequence
Completion criteria	Every agreed channel is either live and recorded, or explicitly marked as not available at this university, and every live channel has its next maintenance task queued
Handoff	To the Portal (ST8) , the moment a student follows the link. The partner row stays open and keeps producing

REQUIRED ACTIONS

1. **Work the plan from ST2, not a template.** The row tells you which channels are open at this university and who agreed to each. A channel nobody agreed to is not on your list.

2. **Activate every agreed channel within two weeks of the meeting.** The advisor is warmest immediately after; a month later you are re-introducing yourself.
3. **Supply ready-to-send copy for anything a partner sends.** The advisor should have to forward, not write. This is the single largest determinant of whether ST6 actually happens.
4. **Mark a channel *not available here* out loud.** A dead job board recorded as dead is useful; a dead job board left blank looks like work nobody did.
5. **Record the distribution when it happens,** being the channel, the date, the asset used, and a rough reach estimate, on the partner row.
6. **Report results back to the partner.** *Your listserv produced eleven applications.* It is the reason they send the second one, and it is the natural moment to ask for the next thing.
7. **Never let a secured channel go unwatched.** Every live channel carries a next check date; working that date is the job.
8. **Re-check the whole row each term.** A row fully activated in September is not necessarily activated in January.

THE FIVE CHANNELS: WHO ACTS, SECURED, MAINTAINED

	Channel	Who acts	Secured means	Maintaining means	Rhythm
ST3	University job board	You post; the advisor or the board's owner approves	The listing is live and visible to students	Check the listing is still up and has not expired or been archived; repost or renew it when it has	Every few months
ST4	Student organisations	You build the relationship; an officer shares it	An officer has shared it once	Refresh the relationship before it goes cold, and re-establish it with the new officers when leadership turns over	Ongoing, and every term
ST5	Campus events	You and the Sales Lead attend	We are registered for a specific event on a specific date	Confirm the event is still scheduled and still on our date; rebook when it moves, and get on the next one after it passes	Before each event, then re-book
ST6	Advisor listservs	You supply the copy; the advisor sends it	The advisor has agreed to send, and has our copy	Remind the advisor to send it, with fresh copy ready each time. The send happens because we asked	Each agreed send
ST7	Professors and class visits	You and the Sales Lead, once permitted	A professor has agreed to an introduction or a visit	Follow up and email professors, its own kind of work, with its own record of who was contacted, who agreed, and which class was visited	Per professor, then per term

Each of these carries specifics the table cannot hold: which board, which officer, which fair and its registration deadline, which list and when it goes out, which professor and which course. That detail belongs on the row against the channel.

ST7 is its own workstream. Professor outreach behaves less like a channel than like a second, smaller outreach funnel: named professors, a permission state on each, an email to follow up, and a class visit to schedule once someone says yes. Scoped and named separately when we get to it, and noted here so it is not mistaken for a checkbox.

WHAT MUST BE RECORDED

Per channel: secured, not yet, or not available here · the named contact · the date live · the next check date · the distribution date, asset used and reach estimate.

Your working state is the set of partner rows with live channels and the date each is next due. That is why the advisor follow-up tab and its queued tasks (**B9**, **B10**) are the difference between five universities and fifty.

[Back to top](#)

WHERE THE PORTAL RUNS AND YOU HANDLE EXCEPTIONS

Four stages the Portal owns. You are here for what the system cannot resolve, not as a step in the flow. Each list below is deliberately short; the master says so explicitly for ST8 and QUAL, on the grounds that if these lists grow the system has failed.

ST8 STUDENT APPLICATION SUBMITTED

Owner: Portal. You are a user *only when the system cannot finish the job*. The student scans the QR code, answers the eligibility check, accepts the Student Caregiver Program Agreement, works the application against a completeness meter, is chased by a fixed ladder of nudges on days 1, 3, 5, 7, then 21, 35, 49, 63, and presses **Go Live**.

PROFILE NUDGES



Eight nudges, then it stops

The completeness ladder. Four nudges in the first week, four more over the following six, then silence.

1. **Watch the stall, not the student.** The ladder handles the individual; what needs attention is the pattern. A campus where half the applications stop at the same section is a broken question or a broken upload, not eight unmotivated students.
2. **Log why students stall**, so the pattern is visible at all.
3. **Intervene by hand only when the system cannot:** a document that will not upload, a student whose circumstances do not fit the form.
4. **Check both entry paths after any change to the assets.** The QR code and the email link must each carry a student all the way through.

Olera

Logan I. Dulose
Abilene, TX

Weekly Availability

No availability set
Add the times you're available each week so providers can match with you.

Availability & Commitment

No availability info
Tell providers about your commitment to caregiving.

Why I Want to Be a Caregiver

No statement yet
Share what drives you to caregiving.

Not live yet
Make your profile visible to providers and start getting matched with jobs.
Go Live

Profile completeness
5%

JUST GETTING STARTED
Complete your application to get matched

- Profile Overview 50%
- Weekly Availability 0%
- Availability & Commitment 0%
- Why I Want to Be a Caregiver 0%
- Screening Questions 0%
- Experience 0%
- Certifications 0%
- Skills 0%
- Resume & LinkedIn 0%
- Verification 0%

Exhibit AB. The application portal. The student's profile section by section, each with its empty state and edit control. On the right, **Not live yet** over the **Go Live** button, and **Profile completeness**. This is the screen behind **B15** and **B16**: nothing on it is required to go live.

QUAL PORTAL VETS THE APPLICATION

Owner: Portal. You are a user *on exceptions*.

1. **Handle exceptions, not cases.** A student the rules would reject who is obviously right, or the reverse. **Record the reason for every override.**
2. **Feed failure reasons back into the application.** A criterion that keeps failing honest applicants is a badly written criterion.
3. **Watch what happens after the list goes out**, whether students actually call, and what providers say when they do. That is the fastest signal we have about whether our bar means anything.

MA1 CANDIDATE INTRO


Owner: Portal, User Success Manager on exceptions.

1. **Send to the provider in the form they will open:** PDF attached, link included, no login asked for.


2. **Do not rely on the board.** If a qualified student has not been introduced anywhere this week, that is a push we failed to send, not a student who failed to look.
3. **Watch the students who are qualified and not yet hired.** That list is the whole job at this stage.
4. **Keep the call list current.** A student calling a provider who is no longer hiring wastes the one thing we are trying to build.

MA2 INTERVIEW HELD

Owner: Portal. You are a user *on exceptions*. The interview state machine runs *proposed*, *confirmed*, *completed*, *cancelled*, *no-show*, *rescheduled*, proposals email the other side, confirmations email both, and a calendar file is attached on confirmation.



Also from confirmed:



Interview states. Two of the three ways out of confirmed are failures worth recording.

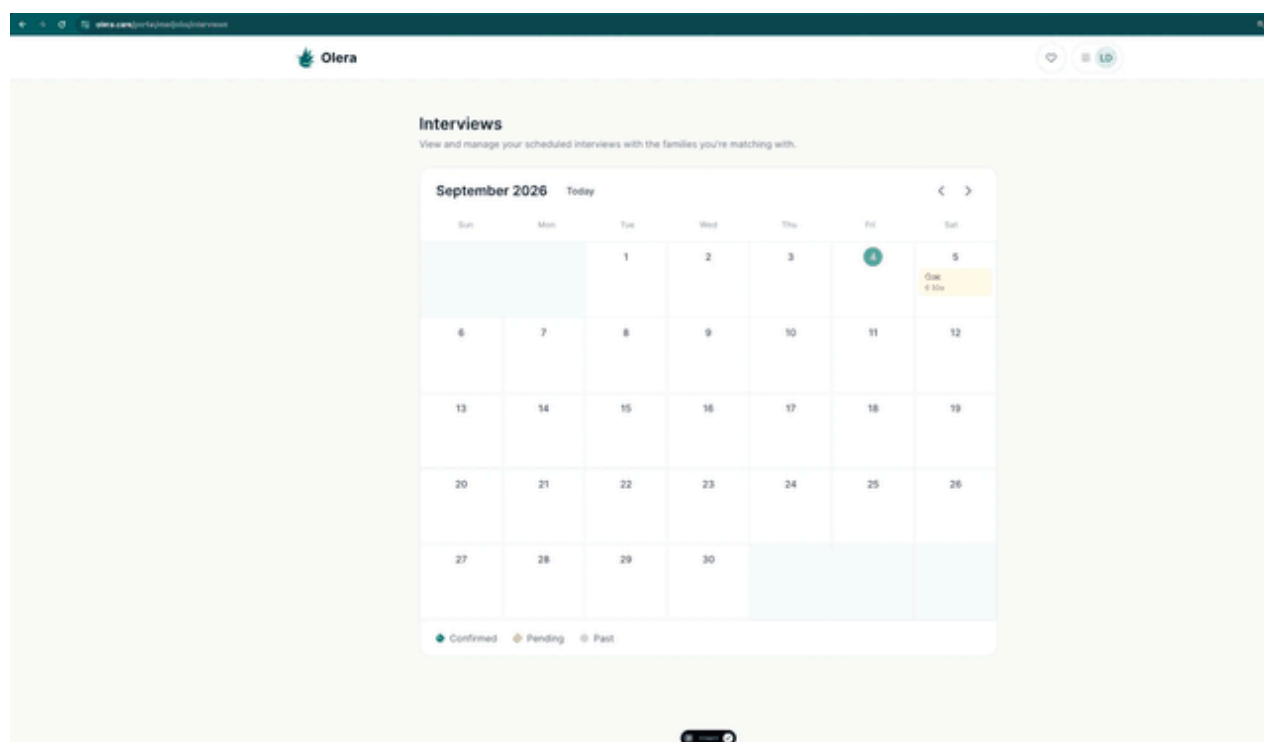


Exhibit AE. The interview calendar with a pending request. The requested interview sits on its date in the amber of **Pending**, waiting on the provider to confirm. **This is the state your first required action is chasing.**

1. **Chase the proposal that has sat unanswered.** A pending request nobody confirmed is the single most common place a match dies.
2. **Confirm by hand when a provider will not use the system**, and put the invite on the calendar anyway.
3. **Ask the student first** whether the interview happened. They answer faster, and it is their outcome.
4. **Record a no-show as a no-show.** It is a different problem from a hire that did not happen, and only one of them is the student's.

[Back to top](#)

MA3 HIRE CONFIRMED

Objective Find out whether the interview produced a job, and if it did not, find out why.

A hire we did not hear about is a hire we cannot bill for. This stage exists because nobody tells us on their own. The provider hires and moves on; the student starts work and moves on. Every placement we know about is one we went and asked for.

Trigger	The interview is confirmed held. Open the cadence the day after
Tools	Nothing is built. SMS, email, the daily call queue and the monthly list call, worked by hand
Communications	Post-interview SMS to the student · follow-up email · the call task when neither lands · a single email to the provider
Completion criteria	A recorded answer either way, with a reason when the answer is no
Handoff	To MA4, on a confirmed hire

REQUIRED ACTIONS

1. **Open the cadence the day after the interview**, while both sides still remember it.
2. **Student first, by SMS.** One question, answerable in four words.
3. **Escalate to a call** when two touches go unanswered.
4. **Ask the provider once**, by email, and do not chase them further. The monthly list call picks up what they did not answer.
5. **Record the reason for every no.** A blank reason is a lost lesson.

WHAT MUST BE RECORDED

Interview outcome, hired or not, start date, the reason when not, and which channel got the answer.


Instrument the no. A hire that did not happen is the most useful signal in the funnel: the interview was a formality, the schedule did not work, the student went quiet, the provider was not really hiring. Without a reason field, this stage produces a number nobody can act on.

[Back to top](#)

MA4 SIX OR MORE SHIFTS WORKED, CONFIRMED

Objective Establish that the placement actually stuck, six shifts worked, because that is the point we bill.

Chase the student, not the provider. The student knows what they worked and answers a text. The provider is the customer, and asking them to do our record-keeping every week is how we become annoying before we become useful.

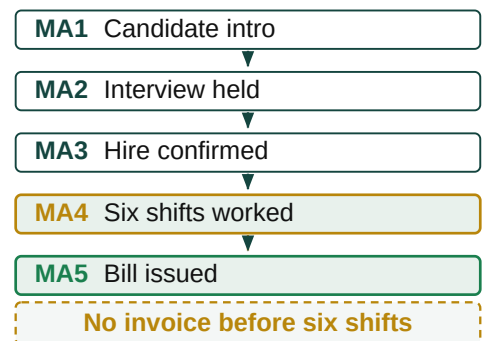

The fulfilment chain. Every stage before MA4 is unpaid work; the six-shift confirmation is what releases the invoice.

Trigger	A hire is confirmed in MA3 and the student has a start date
Tools	SMS on the same stack as MA1 and MA3, and email. The monthly client list call. No shift concept exists in the product
Communications	Student SMS on a rhythm · the same question by email · the monthly client list call
Completion criteria	Six shifts confirmed and recorded against the placement
Handoff	To MA5, once six are confirmed

REQUIRED ACTIONS

1. **Text the student on a rhythm** from their start date until the answer reaches six.
2. **Never ask the provider week to week.** Their confirmation comes on the list call.
3. **Run the list call monthly per client**, every student placed with them, top to bottom.
4. **Record the confirmation and where it came from:** the student, the provider, or both.
5. **Escalate a placement that stalls before six.** A student who stopped after two shifts is a problem worth understanding while it is still fixable.

WHAT MUST BE RECORDED

Shifts worked and the date each was confirmed, who confirmed it, and the list-call record per client.

Comms before a logging surface. A logging surface is more precise and worth building eventually, but a text a student answers beats a form they do not fill in.

[Back to top](#)

MA5 BILL ISSUED AND COLLECTED

Objective Turn a confirmed placement into an invoice, and the invoice into money.

Manual first, deliberately. At current volume raising an invoice by hand is not a stopgap. It is the right answer, and it is how we learn what the automated version should do.

Trigger	Six shifts are confirmed in MA4. The confirmation is the event, not a billing day
Tools	By hand. Eventually a button on the client record, which does not exist yet
Communications	Invoice · receipt · payment reminder · the billing conversation on the list call
Completion criteria	Invoice issued against a confirmed six-shift placement, and payment recorded
Handoff	Complete. The client record carries the history

REQUIRED ACTIONS

1. **Raise the invoice as soon as six is confirmed**, not on a billing day. The confirmation is the event.
2. **Bill against the placement, not the client**, one invoice per student, so a dispute is about one student.
3. **Record payment where the placement lives**, so the client record stays the single account of what happened.
4. **Raise a billing question on the monthly list call**, not by email. The call already exists.

WHAT MUST BE RECORDED

Placement billed, amount, invoice issued and sent, payment received.

[Back to top](#)

THE MONTHLY CLIENT LIST CALL

One recurring commitment, serving two stages at once. The master defines it inside MA4 and points MA3 and MA5 at it.

Rhythm	Monthly per client, or quarterly. The master says monthly in the procedure
What you run	Every student placed with that client, top to bottom: still working, how many shifts, any problems
Why a call	One conversation confirms what a dozen emails would not, and it is a touchpoint rather than an interruption
What it serves	MA4, where the provider confirms shift counts. MA3, where it picks up the hire questions the provider did not answer by email. MA5, where billing questions are raised
What it replaces	Asking the provider week to week. Never do that

The master lists this as **B27**: a practice to establish, not code, and one that needs the client record (**B5**) to run from.

GAPS AND DECISIONS NEEDED

Each of these is a place the master document leaves open or names as unbuilt. None is resolved here. This role carries more of them than the other two, because most of what it owns runs by hand today.

B5 · The client record. The most blocked item in the whole system. One place holding everything after conversion: notes on every touchpoint, plus the interviews, hires, six-shift confirmations and invoices against that client. **PR3, MA4 and MA5 all wait on it**, and so does the monthly list call. An MVP of notes and a timeline would carry the stage.

B4 · An alert when a meeting converts. Nothing tells you a provider is waiting. Until it exists, the Sales Lead naming the handoff in the room is what starts the clock on your one-business-day terms email.

B9 and B10 · The advisor follow-up tab, and maintenance tasks that queue themselves. The five channels as a checklist on the partner row, each secured, not yet, or not available here, with its contact and go-live date; and the board re-check, the listserv reminder, the event date and the officer refresh arriving as ordinary daily work. Neither is built. Activation state lives in meeting notes and in your head, and a channel stays alive only as long as someone remembers it.

B11 and B12 · A professor record for ST7, and channel attribution. ST7 is not yet scoped, and channels are not modelled as distinct entities, so which of the five produced a student cannot be told from results, only from effort.

B15, B16 and B19 · What "live" and "qualified" mean. Nothing is required to go live: the review calls everything *"recommended but not required"* and skips verification, where three of the intended five baseline items sit. The nudge ladder treats 100% completeness as done while the Go Live button requires nothing, so two definitions of *live* disagree. And the catchment broadcast calls a candidate *ready to interview* under our name with no written criteria behind it. These three decide what your exception handling on ST8 and QUAL is exceptions to.

B18 · The call list to the student. On qualifying, every provider hiring near them, with name, area and phone number, and an instruction to call. Not built, and the master calls it *"the important half"* of QUAL. The nearest thing today fires when a *provider* accepts terms, names one provider, and offers a link rather than a number.

B17 · Application source capture. Nothing records how a student found us, which is the other half of why ST3 to ST7 cannot be judged by results.

B20 and B21 · The candidate profile as a PDF, and student SMS. MA1's procedure asks you to send in the form a provider will open and to push qualified students. The PDF renderer is not built, and student SMS is not built, though the SMS stack exists with consent, quiet hours, a queue and a flush job.

B22 and B23 · A real calendar event, and the did-it-happen loop. A calendar file is attached to the confirmation email, which is enough to RSVP and not a shared event. And nothing asks either side whether the interview happened: `completed` and `no_show` exist as states and nothing sets them. That loop is the instrumentation the whole match half of the funnel depends on, which is why MA3 currently starts with you asking by hand.

B24 and B25 · The post-interview cadence and the reason on every no. Neither is built. Nothing asks, so nothing is known, and the most useful signal in the funnel goes uncollected.

B26, B27 and B28 · The shift-count rhythm, the list call, and a shift count on the placement. No concept of a shift exists in the product; the only trace of the threshold is the number behind the guarantee. There is no view of who is approaching six.

B29 · Billing on the six-shift trigger. Two legacy billing paths exist, neither matching this model, and the placements Stripe path is stubbed. Needs **B5**.

B13 and B14 · A content pass over every student-facing asset, and entry-path QA from the QR code and from email. All five assets ship and work end to end; none has had a content pass, and the journey is untested as a journey. This is what ST8 required action 4 is asking you to watch for.

[Back to top](#)

TRACEABILITY

Every section of this manual against its source in the master document. Ownership, sequence, handoffs and completion criteria are carried over unchanged.

This manual	Master document
What client success is	PR3, <i>What client success is</i> , and the not-built note above it
PR3, all of it	PR3 objective, journey table with its Built? column, procedure steps 2 to 7, system and handoff row, communications
ST3 to ST7, all of it	ST3 to ST7 objective, the does-not-close and no-generic-version notes, the who-acts table, procedure steps 1 to 8, the secured and maintaining table, the ST7 workstream note, system and handoff row
Portal exceptions, ST8	ST8 owner line and procedure steps 1 to 4; the nudge ladder
Portal exceptions, QUAL	QUAL owner line and procedure steps 1 to 3
Portal exceptions, MA1	MA1 owner line and procedure steps 1 to 4
Portal exceptions, MA2	MA2 owner line, the state machine, and procedure steps 1 to 4
MA3, all of it	MA3 objective, the hire-we-did-not-hear-about note, procedure steps 1 to 5, the instrument-the-no note, system and handoff row
MA4, all of it	MA4 objective, the chase-the-student note, the comms-first note, procedure steps 1 to 5, system and handoff row
MA5, all of it	MA5 objective, the manual-first note, procedure steps 1 to 4, system and handoff row
The monthly client list call	MA4 procedure steps 2 and 3 and the provider-side-is-a-list paragraph; MA3 procedure step 4; MA5 procedure step 4; deferred build list B27
Gaps	Deferred build list B4, B5, B9 to B29 as cited; ST8 and QUAL notes on the two definitions of live

Nothing was added. No stage, status, threshold, rhythm, channel or tool appears here that is not in the master. **Nothing owned by the User Success Manager was omitted:** PR3, ST3 to ST7, MA3, MA4 and MA5 are carried in full, along with the four Portal stages where the master names you as the exception handler.

One deliberate omission of detail, not of instruction. The student-facing surfaces of ST8, being the flyer, the landing page, the agreement, the job board and the application portal, are described in the master with their exhibits. They are the Portal's, not yours, so this manual carries only your four exception actions over them and points at the master for the rest.

[Back to top](#)
